



CONSTRUCTION UPDATE NOTICE

Weeks of: January 1, 2018 thru the week of January 8, 2018

What to Expect On-Site the Next Two Weeks

Retail Tenants:

L.F. Jennings has commenced work on the tenant fit-out construction of Jersey Mike's and Habit Burger. Both expect to open sometime during the spring of 2018. L.F. Jennings recently completed the fit-out construction work for the FedEx store in Building 1 and has turned that space over to FedEx to complete the fit-out work related to their furniture, fixtures and equipment. Gold's Gym and Burton's Grill continue to work on their fit-out construction with target opening dates within the First quarter of 2018.

Townhomes:

The construction of the 119 townhomes is well underway. The first block of townhomes between Rhode Island Avenue and 47th Street are nearly complete. The remaining townhouse blocks between Rhode Island Avenue and 47th Street are expected to be completed by the end of 2018. Currently, 45 townhomes have been sold.

Parking Structure Progress:

CBG Building Company continues construction on the new multi-level parking structure on parcel E – the building 5 pad site. Cast in place concrete foundation walls and footers have been completed, preparation for slab on grade concrete pours on the eastern portion of the garage has begun. Site-work contractor will continue to remove the remaining surplus stockpile to building pads 7 & 8. Precast garage erection began on December 28 and will continue through February 2018.

CSX Crossing:

The closure of the former ERCO plant parking lot between the Rivertech Court cul-de-sac and Lafayette Avenue will continue until the new bridge is open – estimated to be in spring 2018.

The bridge builder, Shirley Contracting, has completed the sidewalks, landscaping, pavement markings, signage, asphalt paving and roadway approaches. Lighting installation, final grading and site cleanup will continue in the upcoming weeks. This work will continue into the First quarter of 2018. The construction will be monitored to assure compliance with County work hours and noise regulations.

CSX Sound Barrier Wall:

An Agreement was recently executed with CSX to allow the construction of a sound barrier wall along Maryland Avenue north of Wells Run Place. Shirley Contracting anticipates commencement of construction work by the second week of January.

Free Daily Shuttle:


Riverdale Park Station features a FREE daily shuttle from 6:30 a.m. to 9:00 a.m. and 4:30 p.m. to 7:00 p.m. It runs every 15 minutes between Riverdale Park Station, College Park Metro Station and Prince George's Plaza Metro Station. The shuttle stop is located near the main entrance to the Whole Foods Market. Use it for quick and easy access to work, shopping, recreation and regional transit. Visit www.rpstransit.com/shutte for more details.

Route 1 Sidewalk:

Construction of the Route 1 sidewalk connecting the Riverdale Park Station development to Albion Road across the WMATA property is expected to start the week of December 4 and be completed by the First quarter of 2018.

Temporary Hiker/Biker Trail is open!

The site plan below indicates the temporary hiker/biker route.

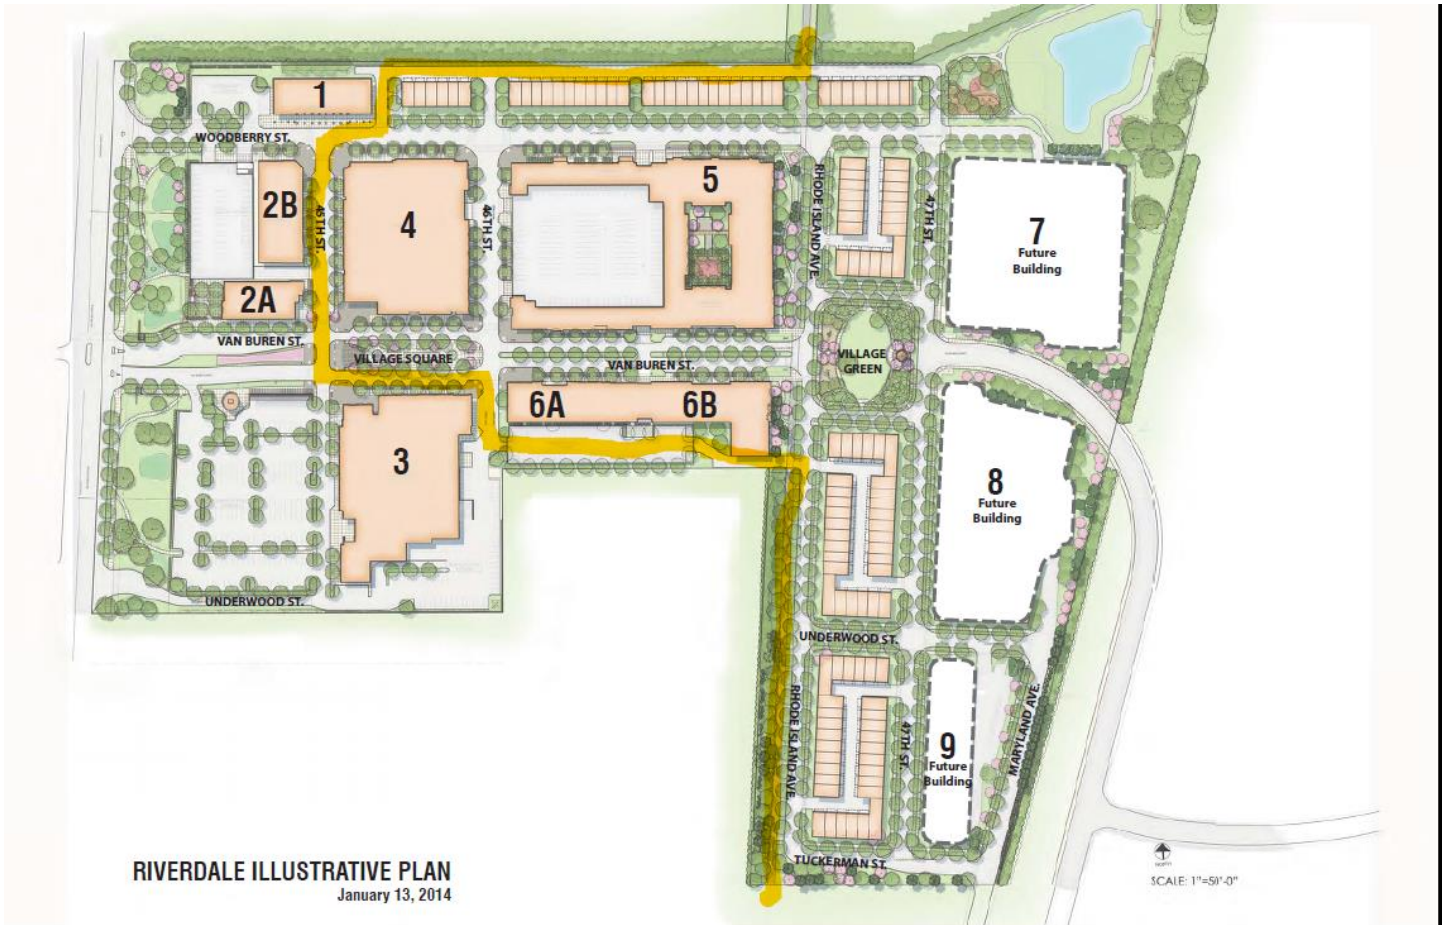

Hikers and bikers should watch for and follow these detour signs:



For more on store openings, events and development news, check out our website and social media pages:

Website: <http://www.riverdaleparkstation.com>

Facebook: Riverdale Park Station

Twitter: @RDPStation

Instagram: rdpstation

Work Hours:

Work activity will be taking place Monday – Sunday between the hours of 7 a.m. and 7 p.m.

Contact Information:

For any **construction related concerns**, please contact Mark Regulinski of Calvin Cafritz Enterprises at 202/248-5806 or email at mark@cafritzenterprises.com.

For **Stanley Martin townhome** information, please contact Brea DePina at 703/939-7039 or email at DePinaBJ@StanleyMartin.com.

Picture Below: Roundabout at Rivertech Court Extension



Picture Below: Landscaping along Rivertech Court Extension



Picture Below: Building 5 Parking Garage Progress – Precast Walls Installation

